
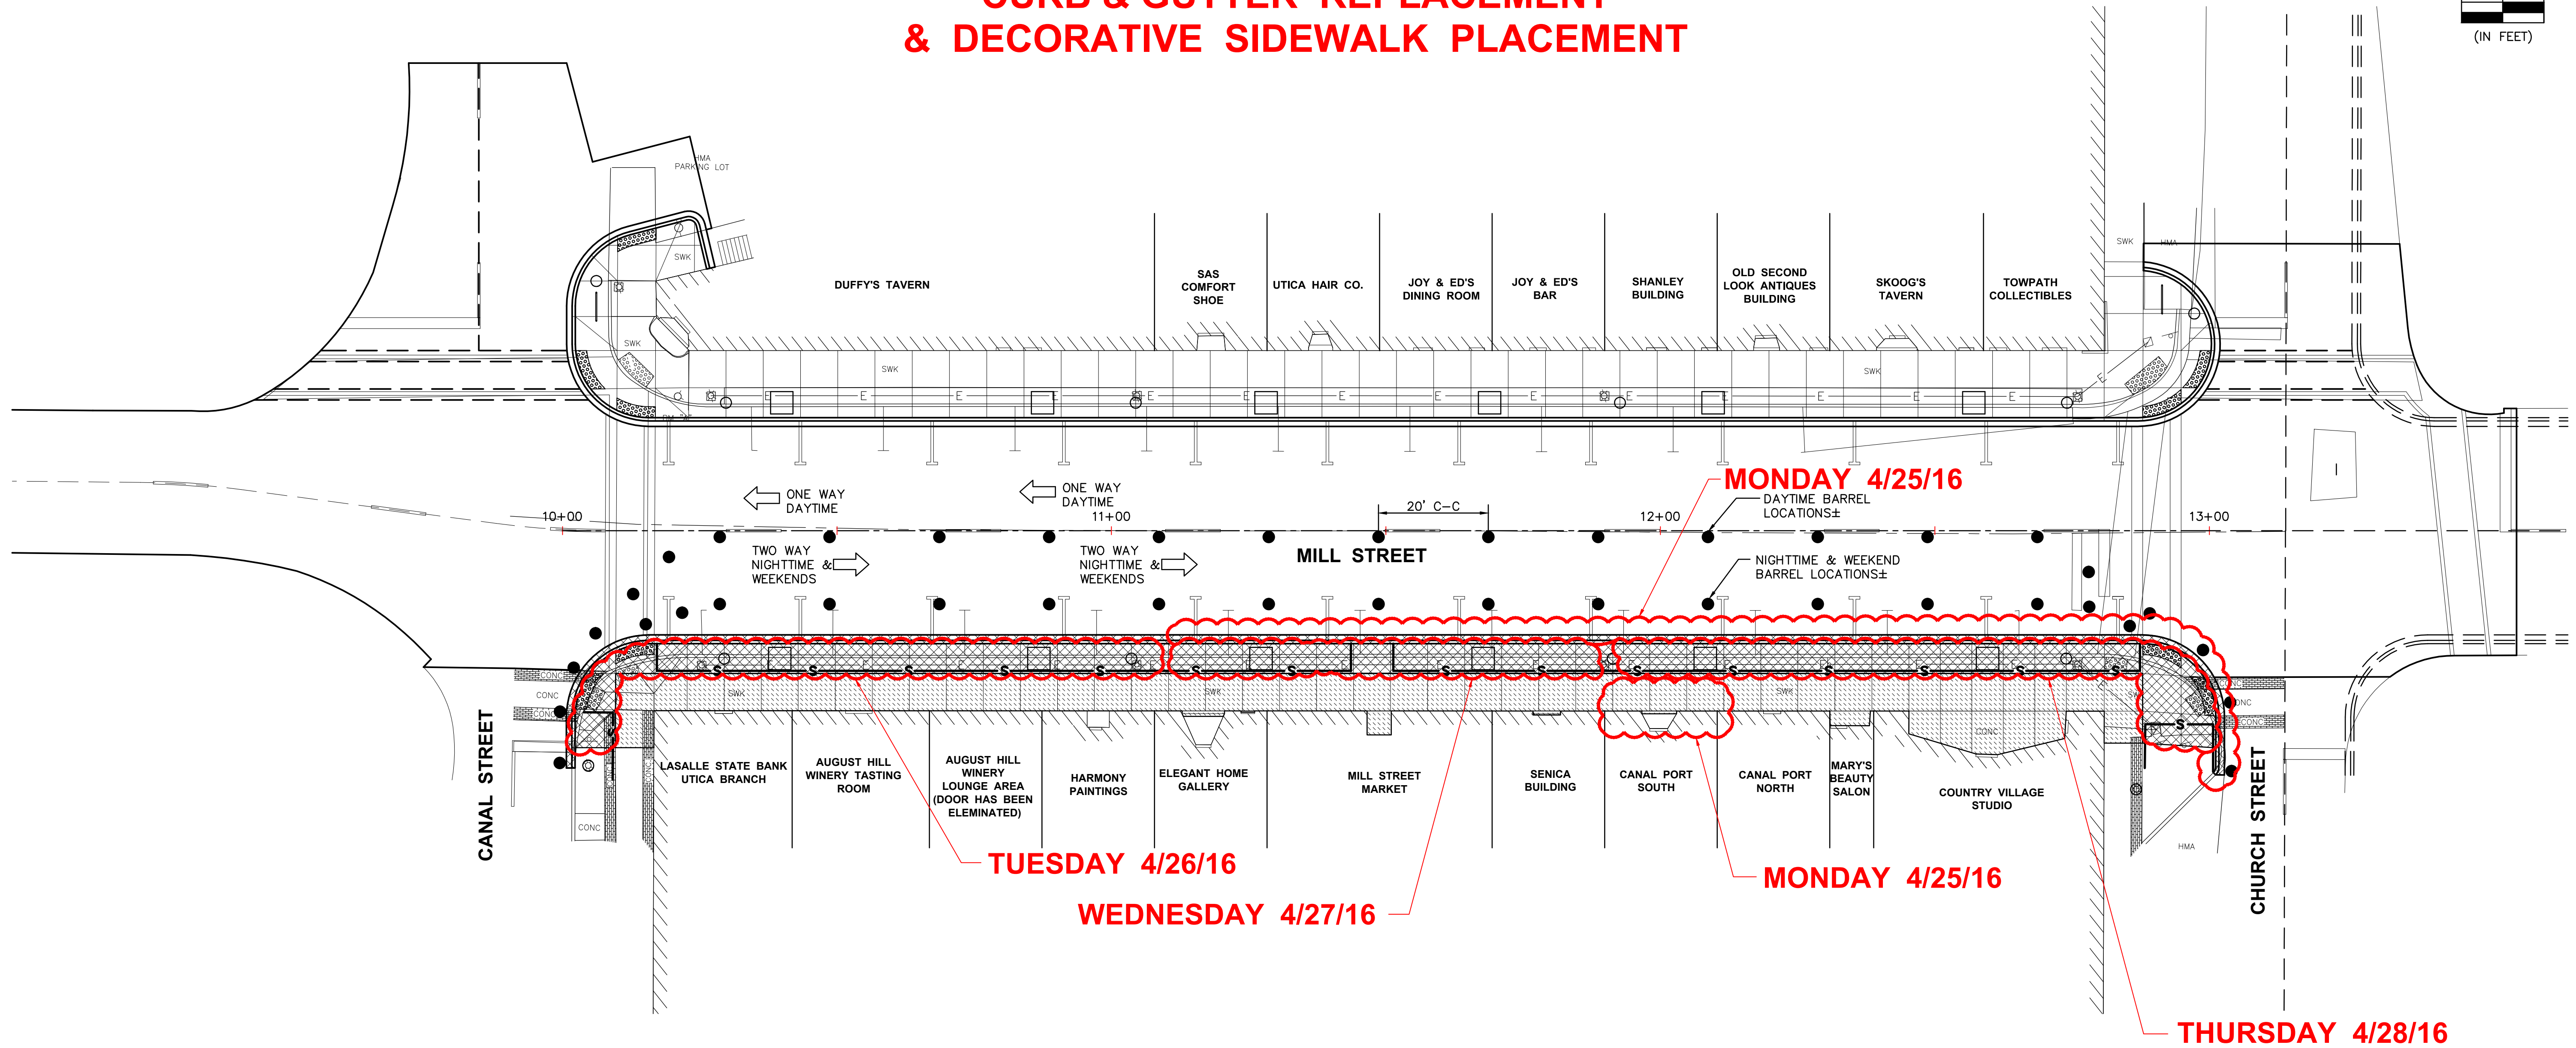


ANTICIPATED WORK SCHEDULE
WEEK OF 4/25/16 - 4/29/16
CURB & GUTTER REPLACEMENT
& DECORATIVE SIDEWALK PLACEMENT



NOTES:

MONDAY WE PLAN TO FINISH THE SIDEWALK IN FRONT OF CANAL PORT AND TO FINISH THE NEW CURB AND GUTTER TO THE NORTH LIMITS IN FRONT OF COUNTRY VILLAGE STUDIOS. THERE IS A CHANCE OF RAIN FOR MONDAY AND IF IT DOES RAIN, WORK WILL BE PUSHED BACK A DAY ACCORDINGLY. WE WILL THEN BEGIN TO POUR THE NEW DECORATIVE SIDEWALK AND HAVE THAT COMPLETED BY END OF WEEK. PROGRESS STANDS AT ABOUT 20% COMPLETION AT THIS TIME.

CHAMLIN & ASSOCIATES, INC. © 2015
Drawing Name: G:\Users\KWH\OneDrive\Projects\2016\Utica\2016 Streetscapes\2016 Streetscapes.dwg
Drawing Date: 04/22/2016
Drawing Time: 4:51pm
Drawing Location: Apr 22, 2016 - 4:51pm
Drawing Status: Printed on: Apr 22, 2016 - 5:23pm by nsej

DRAWN BY: NOE	REVISIONS			
CHECKED BY: KWH	LEVEL	BY	DATE	DESCRIPTION
DATE: 04/16				



PERU MORRIS
ILLINOIS

UTICA 2016 STREETSCAPES
UTICA, ILLINOIS

ANTICIPATED WORK SCHEDULE

CONSTRUCTION
PLANS

CURRENT AS OF: 04/24/2016	
SCALE: AS NOTED	SHEET 1
FILE NO.: 66160.00 Y-	OF 1
