
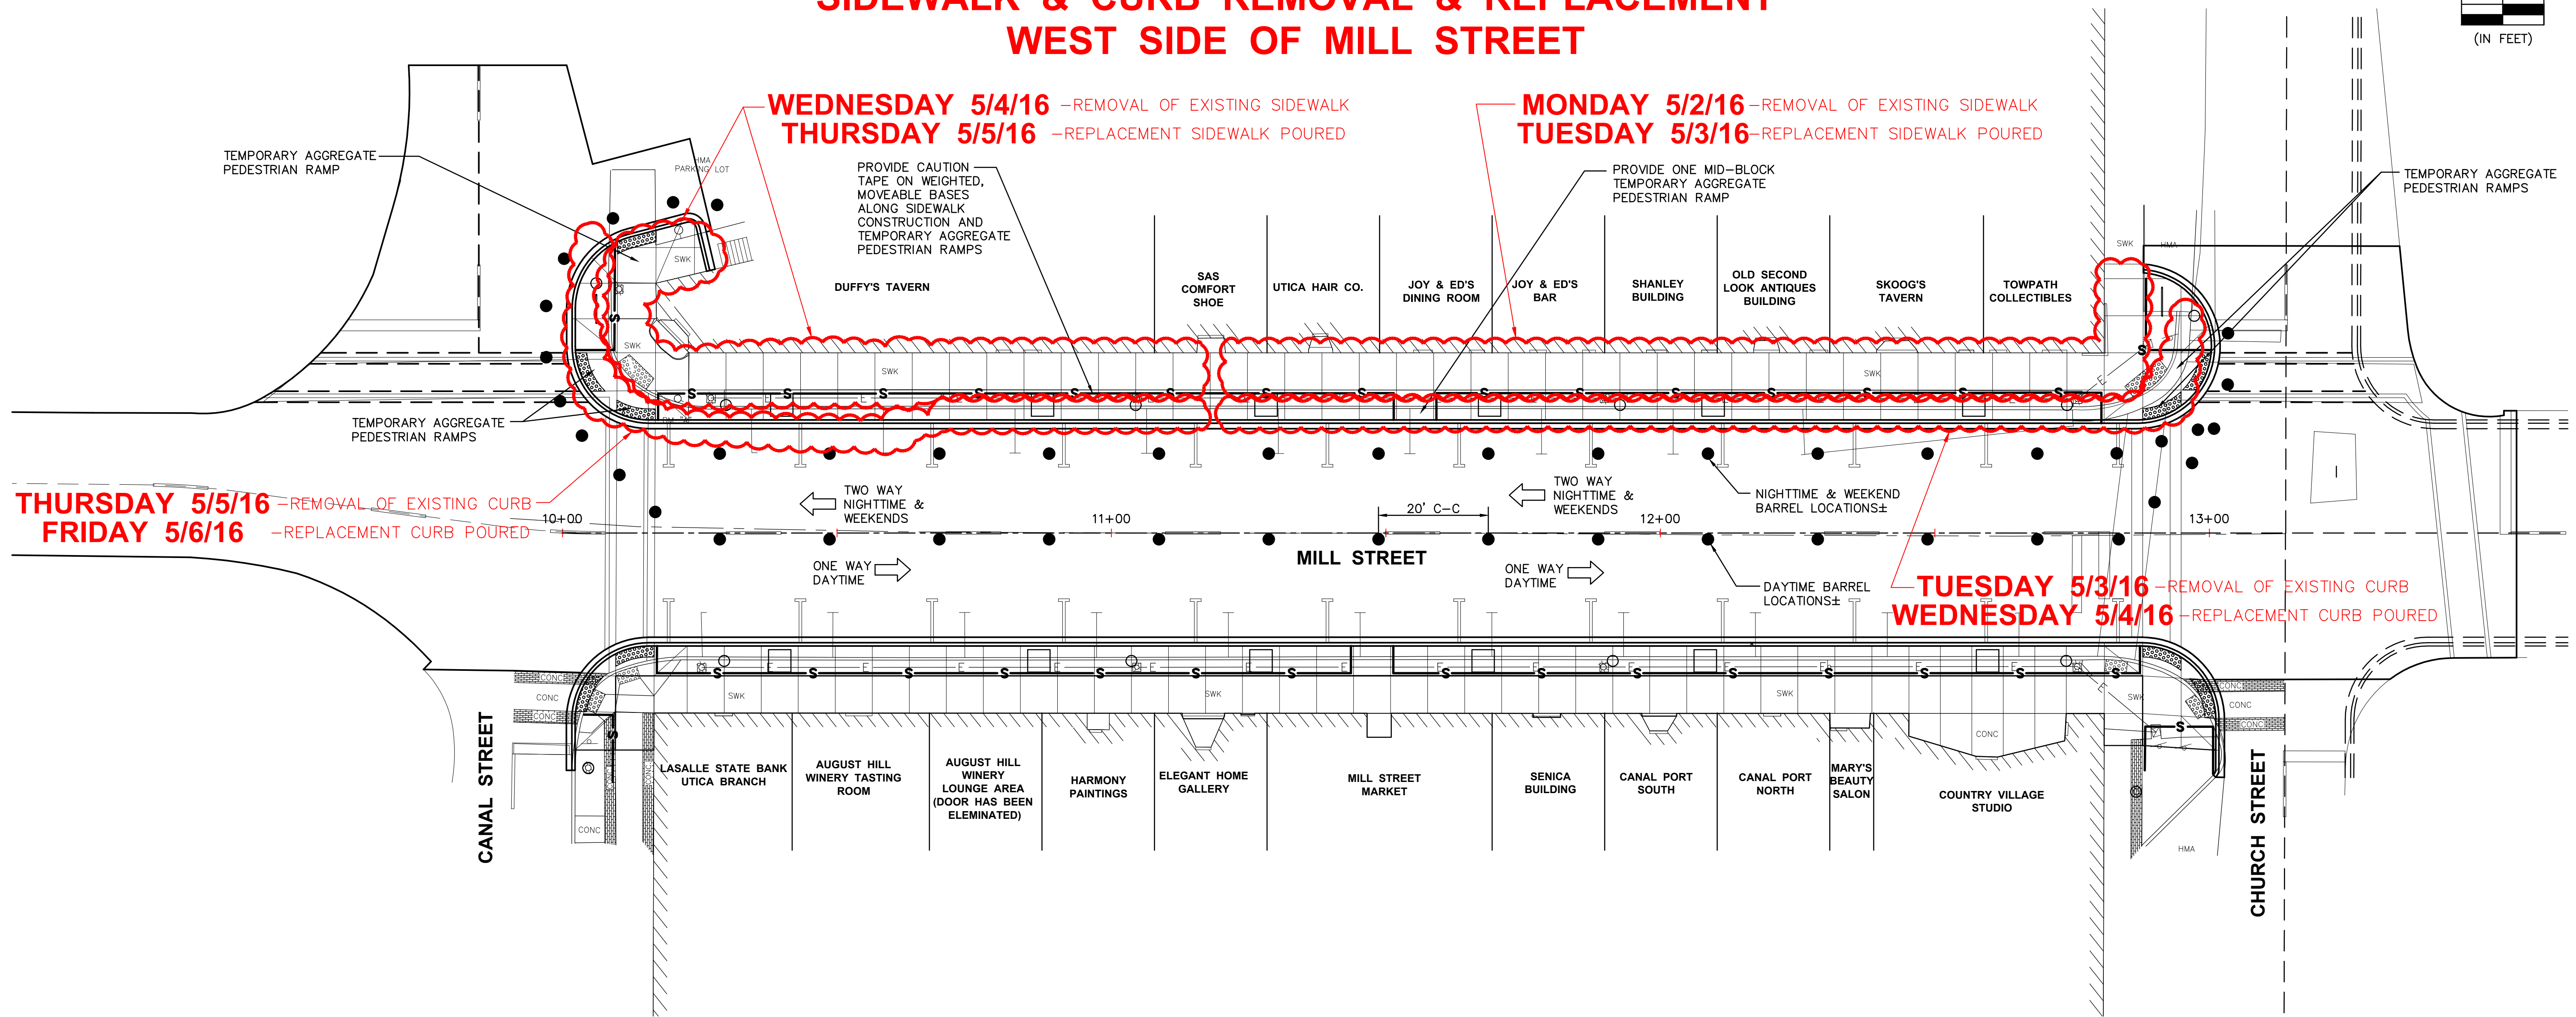


ANTICIPATED WORK SCHEDULE
WEEK OF 5/2/16 - 5/6/16
SIDEWALK & CURB REMOVAL & REPLACEMENT
WEST SIDE OF MILL STREET

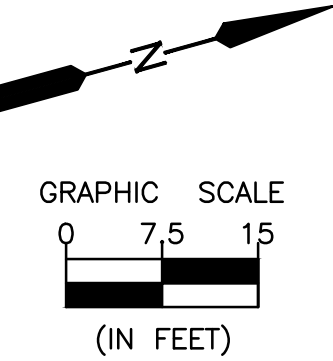

NOTES:

WORK OPERATION WILL SHIFT FROM THE EAST SIDE OF THE STREET TO THE WEST SIDE OF THE STREET. WE WILL INSTALL TWO LIGHT POLES ON THE EAST SIDE OF THE STREET ON MONDAY AND HAVE THEM OPERATING BEFORE THE TWO LIGHT POLES ON THE WEST SIDE ARE TAKEN OUT. THE TREE LOCATIONS ON THE EAST SIDE WILL REMAIN AS IS UNTIL ALL ELECTRICAL WORK IS COMPLETE AT WHICH TIME WE MAY POUR THOSE PANELS. THE PLAN IS TO HAVE ALL SIDEWALK CLOSE TO BUILDING AND NEW CURB DONE BY END OF WEEK WHICH WILL LEAVE ONLY DECORATIVE SIDEWALK TO BE DONE. PROGRESS STANDS AT ABOUT 40% COMPLETION AT THIS TIME.

CHAMLIN & ASSOCIATES, INC. © 2015
Drawing Name: G:\Users\KWH\OneDrive\Projects\2016\2016-15 WEEKLY EXHIBITS-2 TO 5-6.dwg Last Modified: Apr 29, 2016 4:26pm by neq

DRAWN BY: NOE	REVISIONS			
CHECKED BY: KWH	LEVEL	BY	DATE	DESCRIPTION
DATE: 04/16				



PERU MORRIS
ILLINOIS

UTICA 2016 STREETSCAPES
UTICA, ILLINOIS

ANTICIPATED WORK SCHEDULE

CONSTRUCTION
PLANS

CURRENT AS OF: 04/29/2016	
SCALE: AS NOTED	SHEET 1
FILE NO.: 66160.00 Y-	OF 1
