


ANTICIPATED WORK SCHEDULE  
WEEK OF 5/9/16 - 5/13/16  
DECORATIVE SIDEWALK AND  
BEGINNING OF STREET OVERLAY

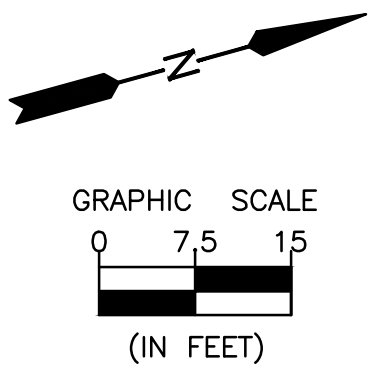

MONDAY 5/9/16 -REPLACEMENT CURB POURED

WEDNESDAY 5/11/16 -DECORATIVE SIDEWALK POURED

TUESDAY 5/10/16 -DECORATIVE SIDEWALK POURED

THURSDAY 5/12/16 -DECORATIVE SIDEWALK POURED

WEDNESDAY 5/11/16 -ADA RAMP POURED

TUESDAY 5/10/16

MONDAY 5/9/16 -ADA RAMP POURED

MILL STREET TO BE MILLED

WEDNESDAY 5/11/16

MILL STREET PRIMED AND LEVEL BINDER PLACED

MILL STREET

CANAL STREET

CHURCH STREET

NOTES:

CONTRACTOR PLANS TO POUR LIGHT POLE BASES MONDAY AND TUESDAY. MILLING OPERATIONS OF MILL STREET WILL BEGIN TUESDAY MORNING AND WILL BE FOLLOWED BY PRIMING THE STREET AND LAYING LEVEL BINDER ON WEDNESDAY MORNING. CONTRACTOR WILL ALSO POUR DECORATIVE SIDEWALK DURING THESE OPERATIONS AS MUCH AS THEY CAN. CONTRACTOR PLANS TO HAVE THE WEST SIDE OF THE STREET DONE BY END OF WEEK LESS THE PANELS WHERE TREES WILL GO. PROGRESS STANDS AT ABOUT 60% COMPLETION AT THIS TIME.

CHAMLIN & ASSOCIATES, INC. © 2015  
Drawing Name: G:\Users\KWH\OneDrive\Projects\2016\06\06160-00-Utica-Downtown-2016\CD\PLANS\PLANS 4-22-16 WEEKLY EXH\5-9 TO 5-13.dwg Last Modified: May 06, 2016 - 3:43pm Plotted on: May 06, 2016 - 3:43pm by noe

DRAWN BY: NOE	REVISIONS			
CHECKED BY: KWH	LEVEL	BY	DATE	DESCRIPTION
DATE: 04/16				



PERU MORRIS  
ILLINOIS

UTICA 2016 STREETScape  
UTICA, ILLINOIS

ANTICIPATED WORK SCHEDULE

CONSTRUCTION  
PLANS

CURRENT AS OF: 05/06/2016	
SCALE: AS NOTED	SHEET 1
FILE NO.: 66160.00 Y-	OF 1
