
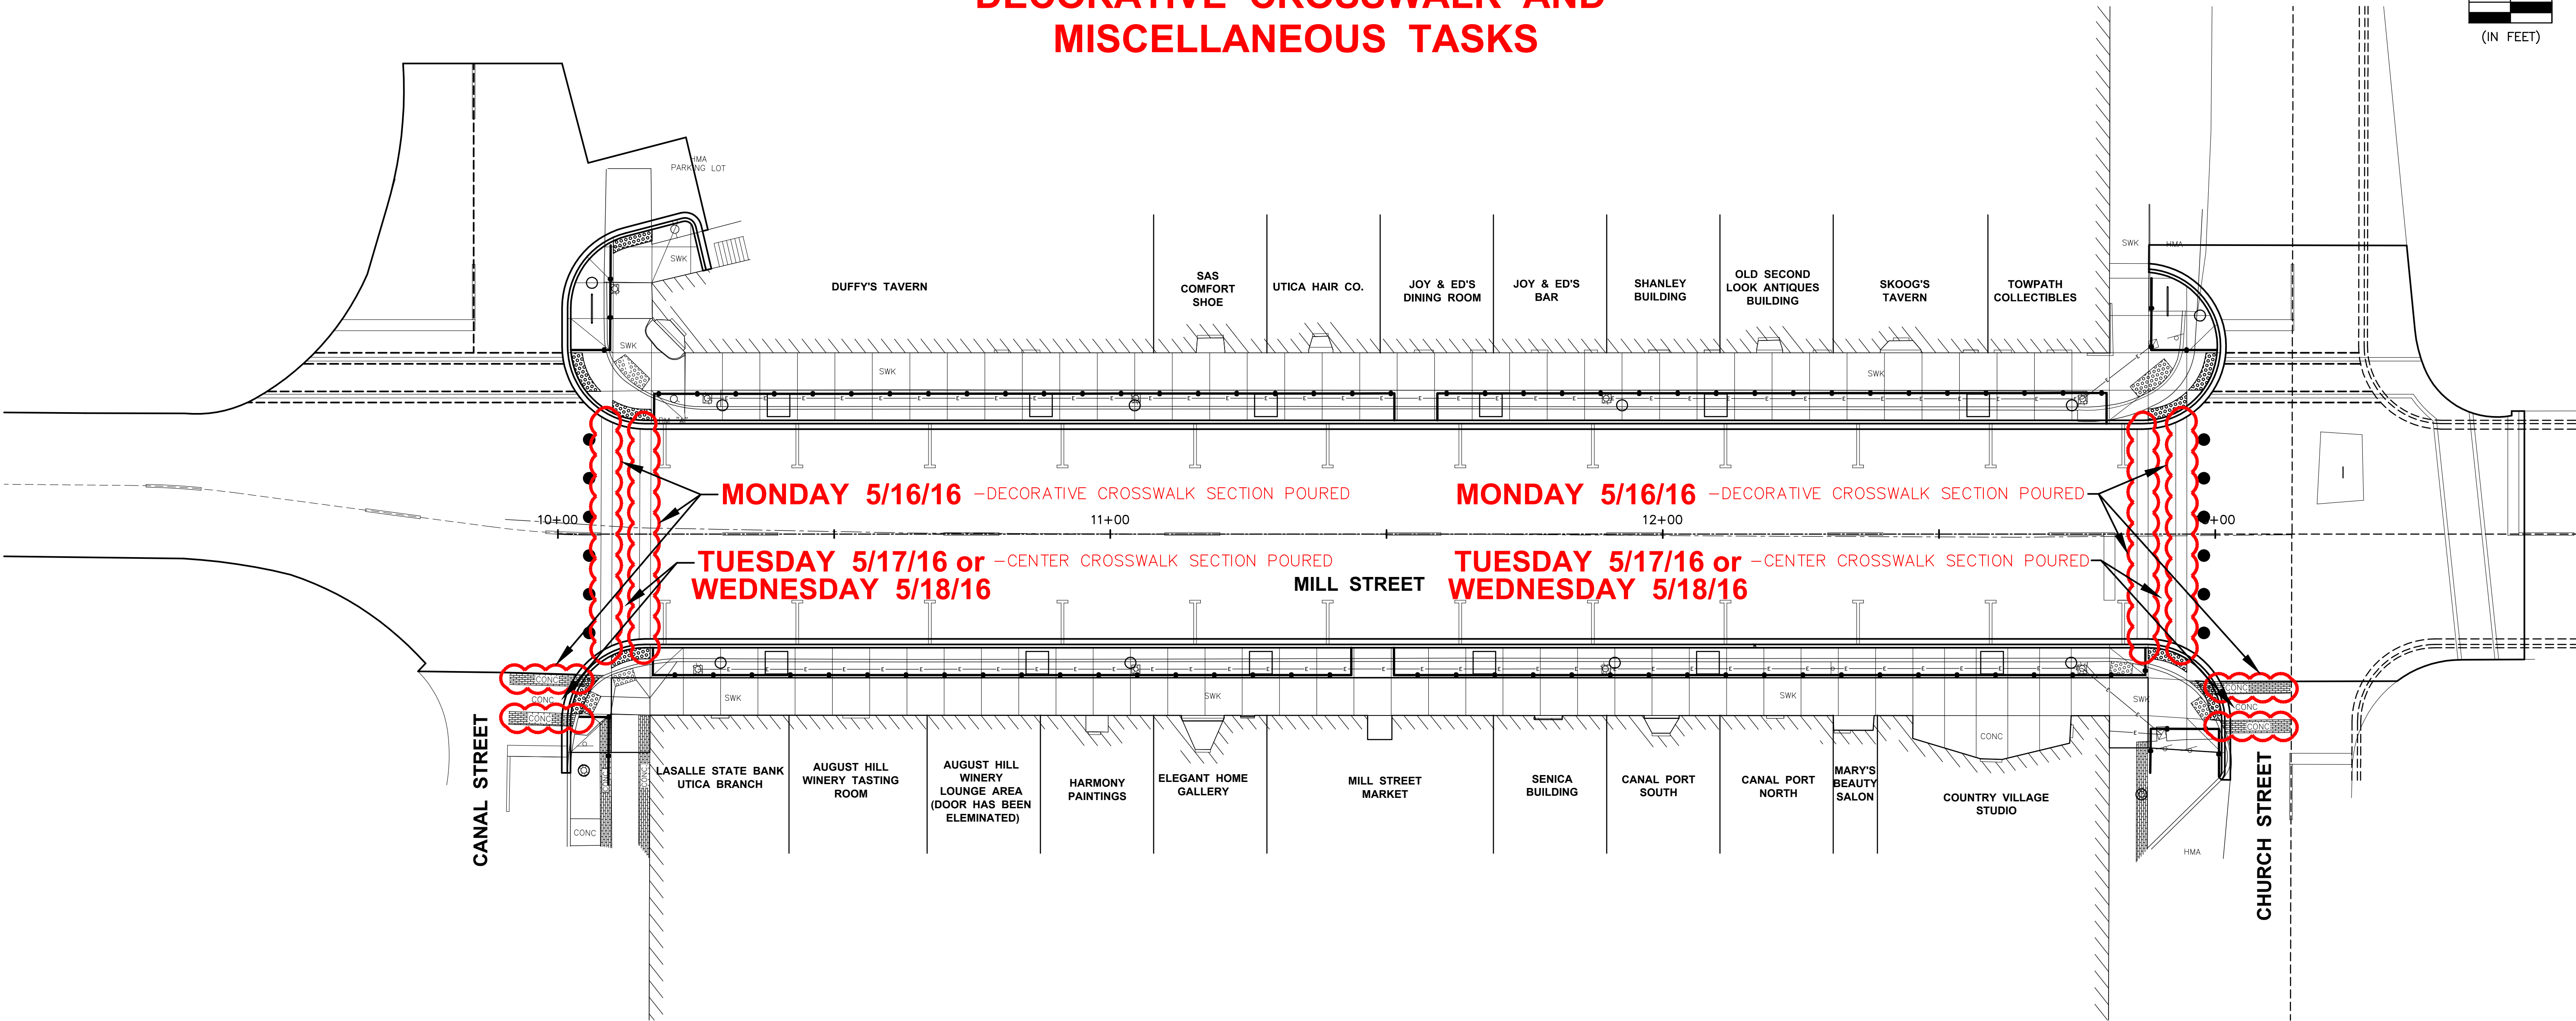


ANTICIPATED WORK SCHEDULE
WEEK OF 5/16/16 - 5/20/16
DECORATIVE CROSSWALK AND
MISCELLANEOUS TASKS

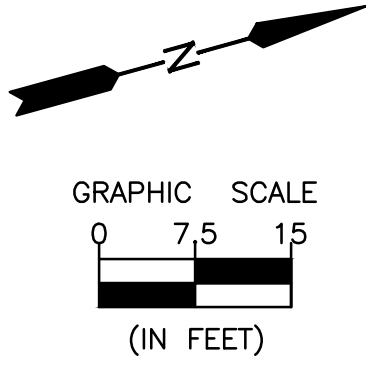

NOTES:

MILL STREET WILL BE CLOSED TO TRAFFIC BEGINNING EARLY MONDAY MORNING. CONTRACTOR PLANS POUR DECORATIVE CROSSWALK SECTIONS ON MONDAY FOLLOWED BY THE CENTER CROSSWALK SECTION ON TUESDAY/WEDNESDAY. ELECTRICIANS WILL BE ON SITE MONDAY TO COMPLETE WIRING AT TREE RING LOCATIONS AND TO INSTALL TWO OTHER LIGHT POLES ON EAST SIDE. CONTRACTOR WILL BEGIN MISCELLANIOUS TASKS SUCH AS CALKING SIDEWALK, OVERLAYING ENTRY SLABS, ETC. WE ANTICIPATE THE STREET CAN BE REOPENED TO TRAFFIC BY THURSDAY IF NOT FRIDAY AT LATEST. PROGRESS STANDS AT ABOUT 80% COMPLETION AT THIS TIME.

CHAMLIN & ASSOCIATES, INC. © 2015
Drawing Name: G:\Users\KWH\OneDrive\Projects\2016\Utica\2016 Streetscape\2016 Streetscape.dwg
Drawing Date: 05/13/2016
Drawing Time: 3:56pm
Drawing User: KWH
Drawing Title: 2016 Streetscape
Drawing Path: G:\Users\KWH\OneDrive\Projects\2016\Utica\2016 Streetscape\2016 Streetscape.dwg
Drawing Size: 11.0 x 17.0
Drawing Scale: 1/8\"=1'-0\"
Drawing Units: Feet
Drawing Color: Black
Drawing Font: Arial, 10
Drawing Plot: Yes
Drawing Plot Date: 05/13/2016
Drawing Plot Time: 3:56pm
Drawing Plot User: KWH
Drawing Plot Title: 2016 Streetscape
Drawing Plot Path: G:\Users\KWH\OneDrive\Projects\2016\Utica\2016 Streetscape\2016 Streetscape.dwg
Drawing Plot Size: 11.0 x 17.0
Drawing Plot Scale: 1/8\"=1'-0\"
Drawing Plot Units: Feet
Drawing Plot Color: Black
Drawing Plot Font: Arial, 10
Drawing Plot Plot: Yes
Drawing Plot Plot Date: 05/13/2016
Drawing Plot Plot Time: 3:56pm
Drawing Plot Plot User: KWH
Drawing Plot Plot Title: 2016 Streetscape
Drawing Plot Plot Path: G:\Users\KWH\OneDrive\Projects\2016\Utica\2016 Streetscape\2016 Streetscape.dwg
Drawing Plot Plot Size: 11.0 x 17.0
Drawing Plot Plot Scale: 1/8\"=1'-0\"
Drawing Plot Plot Units: Feet
Drawing Plot Plot Color: Black
Drawing Plot Plot Font: Arial, 10
Drawing Plot Plot Plot: Yes

DRAWN BY: NOE	REVISIONS			
	LEVEL	BY	DATE	DESCRIPTION
CHECKED BY: KWH				
DATE: 04/16				



PERU MORRIS
ILLINOIS

UTICA 2016 STREETScape
UTICA, ILLINOIS

ANTICIPATED WORK SCHEDULE

CONSTRUCTION
PLANS

CURRENT AS OF: 05/13/2016	
SCALE: AS NOTED	SHEET 1
FILE NO.: 66160.00 Y-	OF 1
